


LAB 2: Agile Backlog Creation & Sprint Simulation in Jira

Student Name: Dhriti Kamani
SRN: PES1UG24AM085

Course: Software Engineering

Project: Smart Hostel Management System

EPIC 2: Ticket Assignment & SLA Management

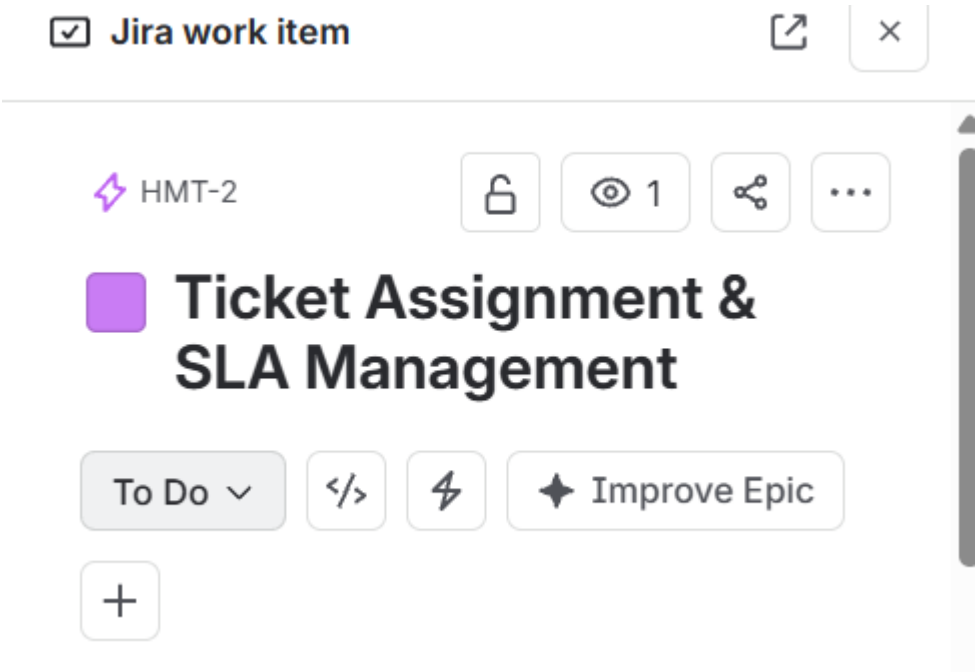

- Description: Allow the Maintenance Warden to view unassigned tickets sorted by severity, assign them to available staff, and set appropriate SLA targets.

Child work items

100% Done

Work	Priority	Assignee	Status
HMT-13 View Unassigned Queue	= Medi...	Unassigned	Done ▾
HMT-14 Assign Ticket to Staff	= Medi...	Unassigned	Done ▾
HMT-15 Auto-populate SLA	= Medi...	Unassigned	Done ▾
HMT-16 Notify Assigned Staff	= Medi...	Unassigned	Done ▾

Total story points = 3+5+3+2 = 13 points

2. User Stories (Detailed)

a) **View Unassigned Queue** - As a Maintenance Warden, I want to see a list of new tickets sorted by severity (High first), so that I can prioritize critical issues.

The screenshot shows a ticket details interface. At the top, there is a blue '+ Create' button, a 'Premium trial' badge, and icons for notifications, help, settings, and a red 'OK' button. Below this is a toolbar with a lock icon, an eye icon with '1', a share icon, and a more options icon. A green 'Done' button with a dropdown arrow, a code icon, a green checkmark with 'Done', and a lightning bolt icon are also present. An 'Improve Story' button is located below the toolbar. The main content area is titled 'Details' and contains the following fields:


Assignee	Unassigned Assign to me
Parent	HMT-2 Ticket Assignment &
Sprint	Add sprint +1
Labels	Add labels
Due date	Add due date
Team	Add team
Start date	Add date
Story point estimate	3

b) **Assign Ticket to Staff** - As a Maintenance Warden, I want to select an available staff member and assign the ticket, so that the right person starts working on it.

This screenshot is identical to the one above, showing the same ticket details interface. The 'Assignee' field is 'Unassigned' with an 'Assign to me' link. The 'Parent' field is '[HMT-2 Ticket Assignment &](#)'. The 'Sprint' field is 'Add sprint +1'. The 'Labels' field is 'Add labels'. The 'Due date' field is 'Add due date'. The 'Team' field is 'Add team'. The 'Start date' field is 'Add date'. The 'Story point estimate' field is '5'.

c) **Auto-populate SLA** - As a Maintenance Warden, I want the system to suggest an SLA based on severity, so that response times are consistent.

Sprint 2

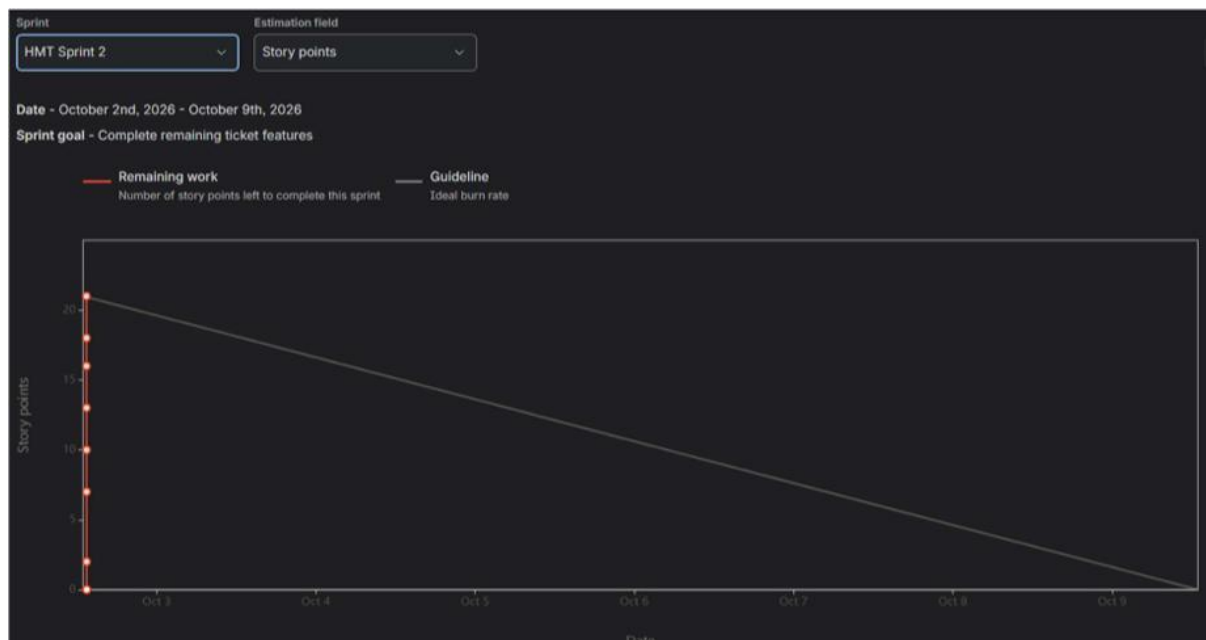

3. Reflect on Answers

1. Did your estimates reflect the actual effort?

Yes, the estimates largely reflected the actual effort. The story points were assigned using the Fibonacci scale during a Planning Poker session with the team. "Log New Ticket" (HMT-9) received 5 points because it required designing the form, validation logic, and database integration. "Auto-fill Room Tag" (HMT-10) and "Attach Photo Evidence" (HMT-11) each received 3 points as they were moderately complex but independent features. "Ticket Confirmation" (HMT-12) received 2 points as it was a relatively simple notification and ID generation task. Upon completing the sprint, the team found that HMT-11 (photo upload) took slightly longer than anticipated due to file size handling and storage considerations, suggesting it could have been estimated at 5 points. However, overall the estimates were within an acceptable range for a first sprint.

2. Was your backlog well-prioritized?

The backlog was well-prioritized for a minimum viable product (MVP). All four user stories were marked as Medium priority because they collectively form the core ticket logging feature. HMT-9 (Log New Ticket) was placed at the top as it is the foundational story — without it, the other stories cannot function. HMT-10 (Auto-fill Room Tag) followed as it improves user experience and reduces friction. HMT-11 (Attach Photo Evidence) came next as it enhances the quality of the ticket but is not strictly essential for basic functionality. HMT-12 (Ticket Confirmation) was last as it is a feedback mechanism that depends on the successful creation of a ticket. In future sprints, we would prioritize based on user feedback and business value more granularly.

3. How did your simulated sprint align with your plan?

The simulated sprint aligned well with the plan. All four user stories were moved from To Do to In Progress to Done within the one-week sprint duration. The team was able to complete all 13 story points, meeting the sprint goal of delivering a functional ticket logging feature. There were no major blockers, though the team noted that the photo upload task required additional testing. The sprint board showed a clean progression, and the burndown chart indicated steady progress with a slight

plateau mid-sprint during the photo upload implementation, which was resolved by the end of the week.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart revealed that the team's capacity for a one-week sprint is approximately 13 story points. The chart showed a relatively linear decline, indicating consistent daily progress. There was a noticeable flat period around days 3–4, which corresponded to the photo upload feature where the team encountered technical uncertainty around image compression and storage. This insight suggests that for future sprints, the team should either allocate more time for technically uncertain tasks or break them into smaller subtasks. The burndown chart also confirmed that the team finished all committed work by the end of the sprint, which is a positive sign for sprint planning accuracy. For the next sprint, the team can consider committing to 15–16 story points based on this baseline capacity.
